


6月度進捗状況

(1) 実 施 工 程				工事概要 φ100 DIP-E(GX) L=588.5m φ50PE L=279m				浦 上 建 設 株 式 会 社																																						
工 事 名 : 配水管布設工事(週休2日)				工 期 自 令和 8年 3月 17日				現場代理人 西 口 徹																																						
岡崎市河原町地内				至 令和 9年 3月 12日																																										
工 種 ・ 項 目	数 量 (単位)	構成比率 (金額) %	月	4月			5月			6月			7月			8月			9月			10月			11月			12月			1月			2月			3月			摘 要						
			日	10	20	30	10	20	31	10	20	30	10	20	31	10	20	31	10	20	31	10	20	30	10	20	31	10	20	31	10	20	28	10	20	31										
準 備 工	1.0 式	5.0%	100 %	実地	100(5.0)																																									
				計画	100(5.0)																																									
φ100布設工	600.7 m	21.3%	90 %	実地							2.5(0.5)																																			
				計画							5.0(1.1)			30.1(7.0)			70.1(14.9)			100(21.3)																										
φ50布設工	279.0 m	8.4%	80 %	実地							2.5(0.2)															70(5.9)			100(8.4)																	
				計画							10(0.6)			30(1.9)			50(3.2)			70(4.5)			90(5.8)			100(6.4)																				
仕切弁設置工	23.0 箇所	6.4%	70 %	実地							50(1.5)																																			
				計画							100(2.2)																																			
消火栓設置工	2.0 箇所	3.0%	60 %	実地				100(2.2)																																						
				計画				100(5.3)			100(5.3)																																			
離脱防止金具設置工	2.0 箇所	2.2%	50 %	実地							20(2.0)			40(4.0)																																
				計画	5(0.5)			35(2.3)			65(6.6)			20(1.0)																																
不断水バルブ設置工	5.0 箇所	5.3%	40 %	実地							30(1.1)			70(2.2)																																
				計画																																										
給水管切替工	50.0 箇所	6.5%	30 %	実地							10(0.4)			15(0.6)			30(1.1)			45(1.7)			60(2.3)			75(2.9)			90(3.4)			100(3.8)														
				計画							10(0.8)			20(1.6)			30(2.5)			40(3.3)			50(4.1)			60(4.9)			70(5.7)			75(6.2)														
仮設配水管工	1,559.3 m	10.1%	20 %	実地																																										
				計画																																										
仮設給水管工	50.0 箇所	3.6%	10 %	実地																																										
				計画																																										
舗装復旧工	2,220.0 m ²	11.2%	0 %	実地																																										
				計画																																										
付帯工	1.0 式	3.8%		実地																																										
				計画																																										
交通誘導工	1.0 式	8.2%		実地																																										
				計画	2(0.2)			10(0.8)			20(1.6)			30(2.5)			40(3.3)			50(4.1)			60(4.9)			70(5.7)			75(6.2)																	
後片付け工	1.0 式	5.0%		実地																																										
				計画																																										
				実地																																										
				計画																																										
				実地																																										
				計画																																										
				実地																																										
				計画																																										
全 体 （ 金 額 ） 工 程		100%	計画		5.7			9.9			26.7			35.3			45.9			56.5			65.1			79.7			86.0			92.0			98.0			100								
			実績		5.0			15.3			20.2																																			
記 事 (指示・検討・是正事項)																																														

配水管布設工事（週休2日） 河原町地内 6月度進捗状況及び7月度施工予定箇所

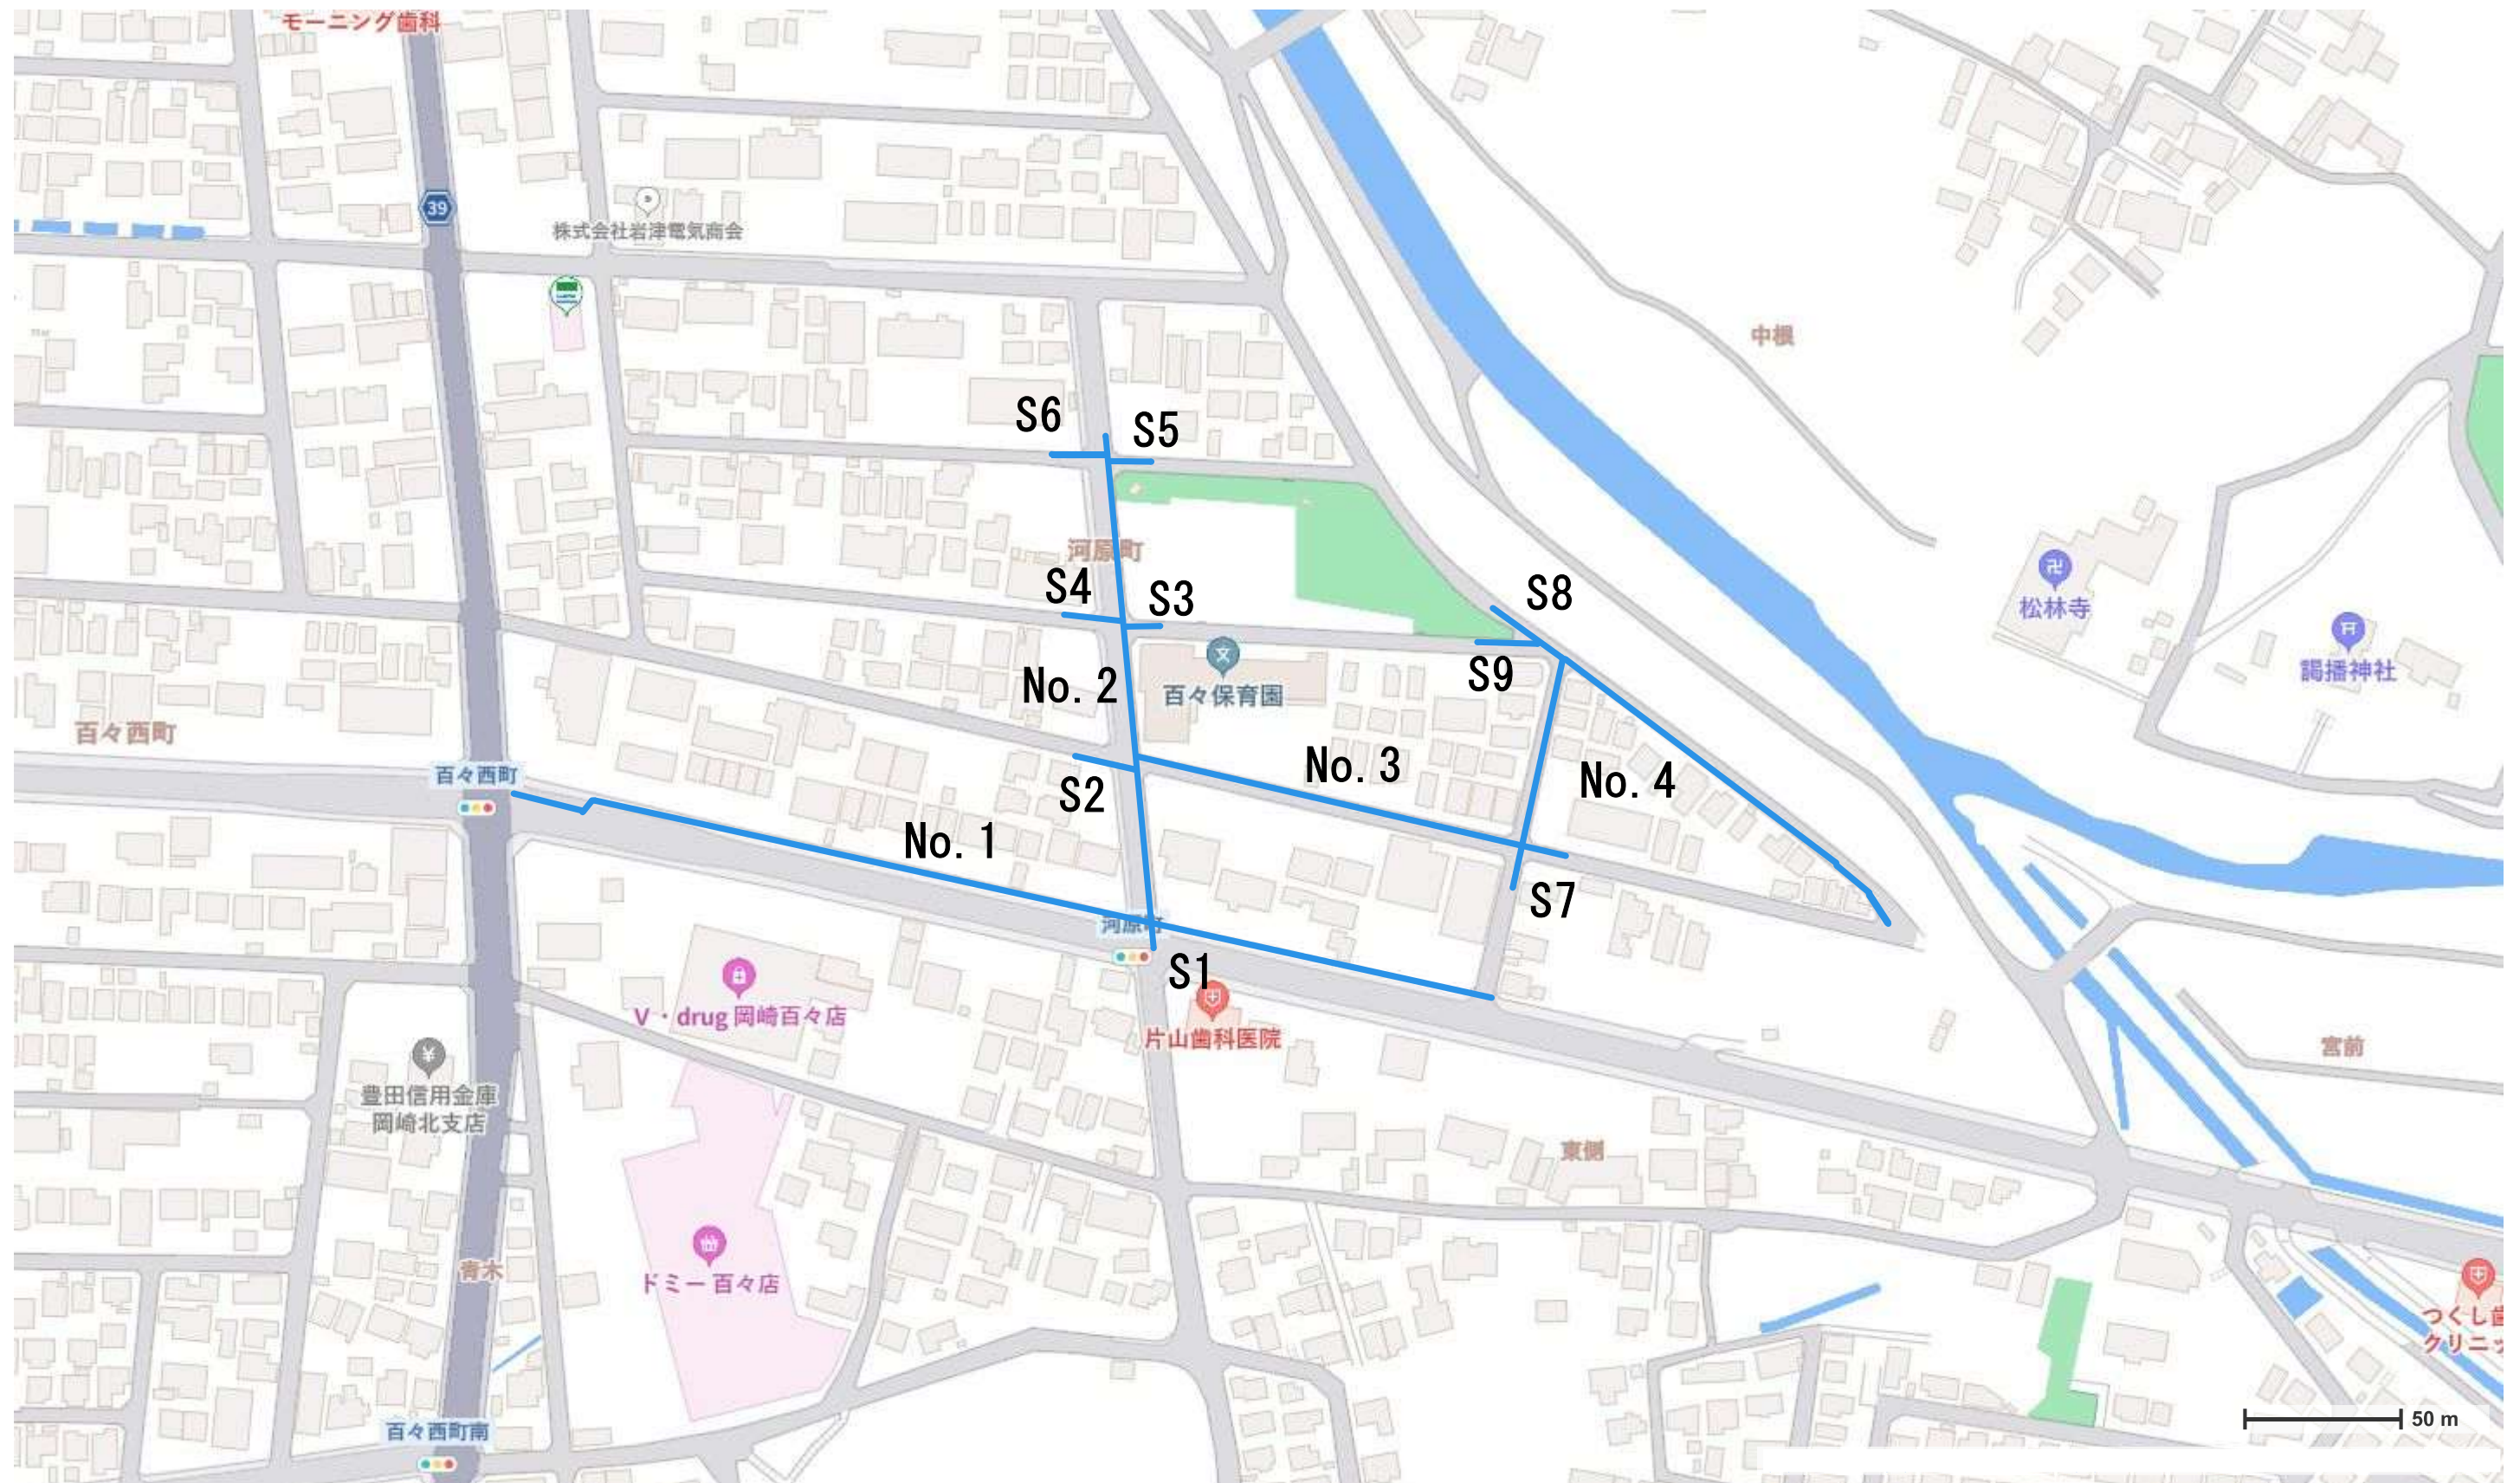

- 施工予定箇所
- 施工完了箇所
