


浦上建設株式会社 配水管布設工事（週休2日）河原町地内

9月度進捗状況

(1) 実 施 工 程			工事概要		φ100 DIP-E(GX) L=588.5m φ50PE L=279m												浦 上 建 設 株 式 会 社																								
			工 事 名：		配水管布設工事(週休2日)		工 期		自 令和 8年 3月 17日				至 令和 9年 3月 12日				現場代理人 西口 徹																								
			岡崎市河原町地内																																						
工 種 ・ 項 目	数 量 (単位)	構成比率 (金額) %	月	4月			5月			6月			7月			8月			9月			10月			11月			12月			1月			2月			3月			摘 要	
			日	10	20	30	10	20	31	10	20	30	10	20	31	10	20	31	10	20	31	10	20	30	10	20	31	10	20	31	10	20	28	10	20	31					
準 備 工	1.0 式	5.0%	100 %	実地	100(5.0)																																				～ 凡 例 ～ 施工進度管理(各月毎) — … 予 定 (黒) — … 変更予定(緑) — … 実績(赤) 全体工程管理 — … 予 定 (黒) — … 変更予定(緑) — … 実績(赤)
φ 100布設工	600.7 m	21.3%	90 %	実地							2.5(0.5)						50(10.7)			60(12.6)																					
φ 50布設工	279.0 m	8.4%	90 %	計画							5.0(1.1)			30.1(7.0)			70.1(14.9)			100(21.3)																					
仕切弁設置工	23.0 箇所	6.4%	80 %	実地							2.5(0.2)			10(0.8)			20(1.7)						70(5.9)			100(8.4)															
消火栓設置工	2.0 箇所	3.0%	80 %	計画							10(0.6)			30(1.9)			50(3.2)			70(4.5)			90(5.8)			100(6.4)															
消火栓設置工	2.0 箇所	3.0%	80 %	実地													50(1.5)			100(3.0)																					
離脱防止金具設置工	2.0 箇所	2.2%	70 %	計画				100(2.2)			100(2.2)																														
離脱防止金具設置工	2.0 箇所	2.2%	70 %	実地				100(5.3)																																	
不断水バルブ設置工	5.0 箇所	5.3%	60 %	計画				100(5.3)																																	
給水管切替工	50.0 箇所	6.5%	60 %	実地																20(1.3)																					
給水管切替工	50.0 箇所	6.5%	60 %	計画																			70(4.6)			100(6.5)															
仮設配水管工	1,559.3 m	10.1%	50 %	実地				20(2.0)			40(4.0)			65(6.6)																											
仮設配水管工	1,559.3 m	10.1%	50 %	計画	5(0.5)			35(2.3)			65(6.6)															90(9.1)			100(10.1)												
仮設給水管工	50.0 箇所	3.6%	50 %	実地							20(1.0)			70(2.2)																											
仮設給水管工	50.0 箇所	3.6%	50 %	計画				30(1.1)			70(2.2)															90(3.2)			100(3.6)												
舗装復旧工	2,220.0 m ²	11.2%	40 %	実地																			50(5.6)																		
舗装復旧工	2,220.0 m ²	11.2%	40 %	計画																						50(5.6)															
付帯工	1.0 式	3.8%	30 %	実地				10(0.4)			20(0.8)			30(1.1)			40(1.5)			75(2.9)			90(3.4)			100(3.8)															
付帯工	1.0 式	3.8%	30 %	計画				15(0.6)			30(1.1)			45(1.7)			60(2.3)			75(2.9)			90(3.4)			100(3.8)															
交通誘導工	1.0 式	8.2%	30 %	実地				10(0.8)			20(1.6)			30(2.5)			40(3.3)			50(4.1)																					
交通誘導工	1.0 式	8.2%	30 %	計画	2(0.2)			10(0.8)			20(1.6)			30(2.5)			40(3.3)			50(4.1)			60(4.9)			70(5.7)			75(6.2)												
後片付け工	1.0 式	5.0%	20 %	実地																																					
			20 %	計画																																					
			10 %	実地																																					
			10 %	計画																																					
			0 %	実地																																					
			0 %	計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					
				計画																																					
				実地																																					

配水管布設工事（週休2日） 河原町地内 9月度進捗状況及び10月度施工予定箇所

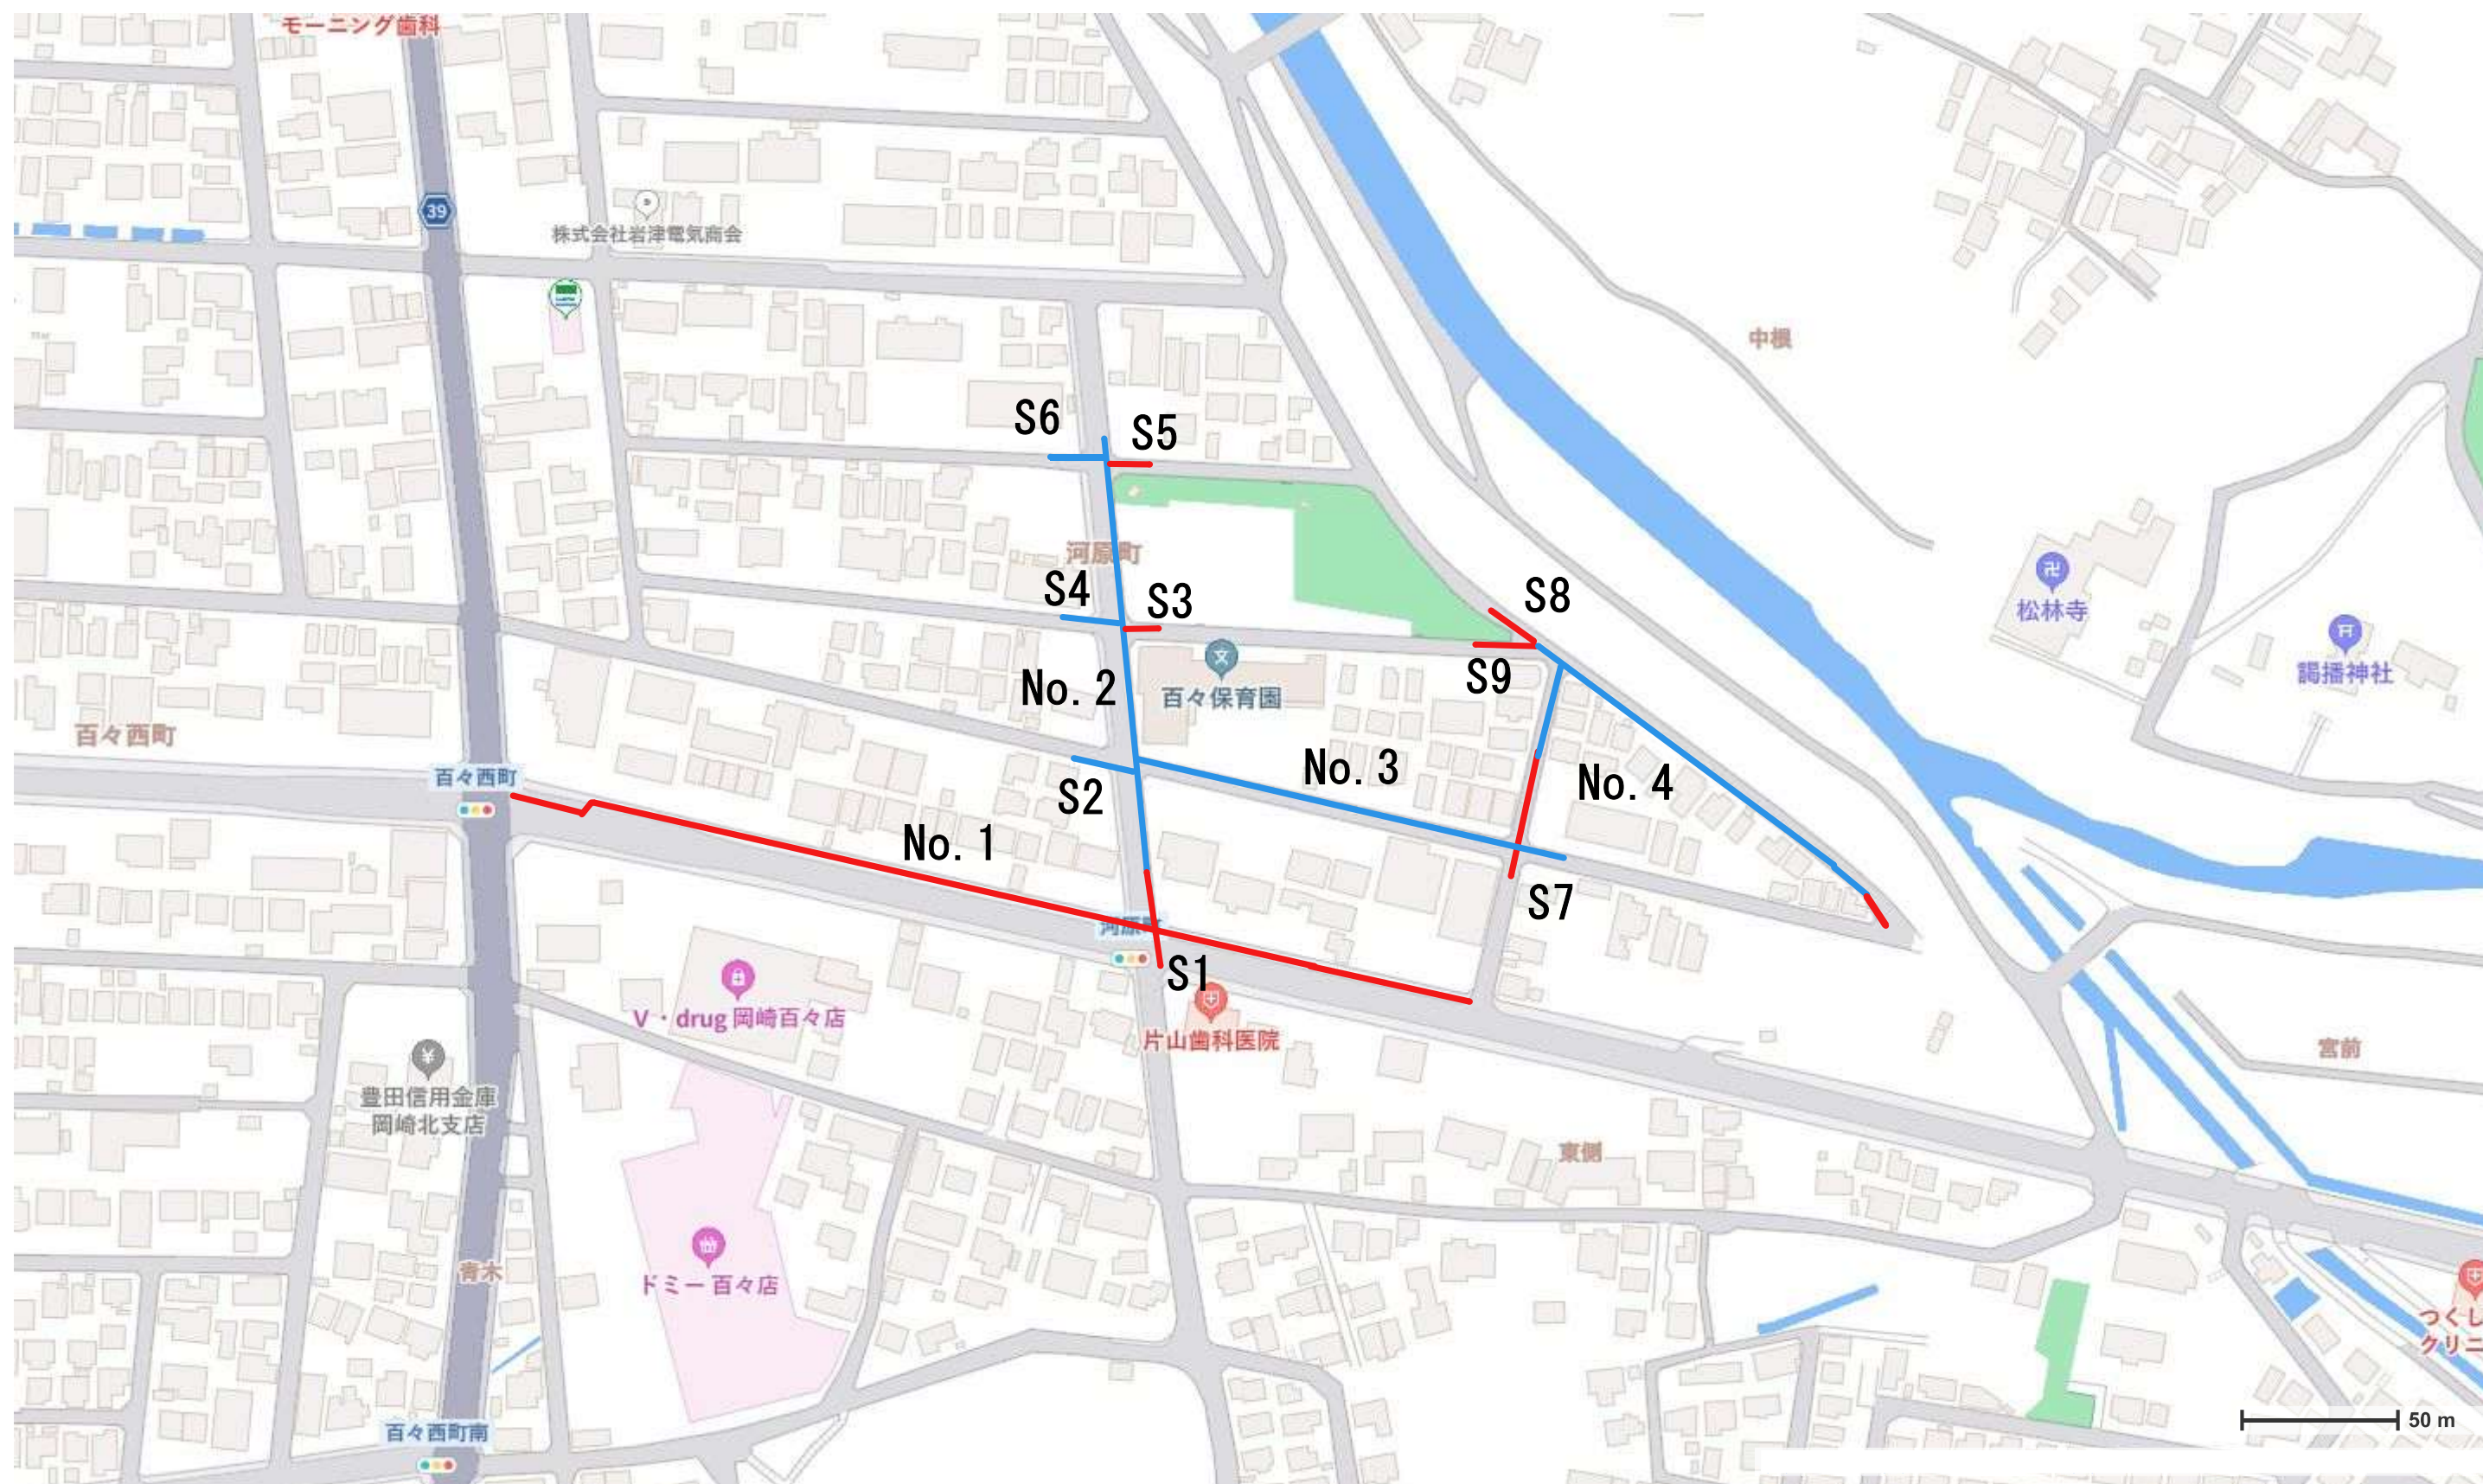

- 施工予定箇所
- 施工完了箇所
